

SVR3 EWP Stream Restoration

Project Weekly Construction Notes: 10/27 to 11/3/2017



Date: 11/03/2017

By: Sharla Lovern – Boulder County Project Manager

Location: St. Vrain Reach 3 – Hygiene Road Work Site

Project Sponsor: Boulder County

Work in Progress/Completed:

1. Installing perimeter fencing to minimize future site disturbance: Gage, Hepp, and Ramey;
2. Survey at Gage, Hepp, Ramey;
3. Silt fence installation at Gage;
4. 10-31-17 Meeting with Martin Marietta Material, ACC and BCPOS to review Breach 2 access agreement;
5. SHPO Discovery Plan training 11-01-17 by NRCS and BCPOS for ACC Operators;
6. Excavation of VTC locations at Hepp and Gage;
7. Installation of rock for VTC at Hepp and Gage;
8. Access gate widening at Hepp.

Upcoming Work:

1. Mobilization of equipment and personnel;
2. Continued survey of in-stream work locations and topo;
3. Clearing and grubbing to get ready for instream-work at Gage and 7a breach repair at Hepp;
4. Water rights acquisition;
5. Traffic signage installation and project signage installation.



11-03-17: Installation of rock for Gage access road improvement and VTC installation



11-02-17: Project signage installation with web site www.BoulderCountyOpenSpace.org/sv3

St. Vrain Reach 3 Restoration Project: Project Weekly Construction Notes: 10/27 to 11/3/2017



11-3-17 Widening of gate at Hepp access point



10-27-17 Silt fence installed at Gage property (Hygiene Rd Access to South)




11-01-17 Washed VTC and equipment delivery at Hepp



10-27-17 Construction perimeter fencing and first wood delivery at Ramey access point near 61st

St. Vrain Reach 3 Restoration Project: Project Weekly Construction Notes: 10/27 to 11/3/2017

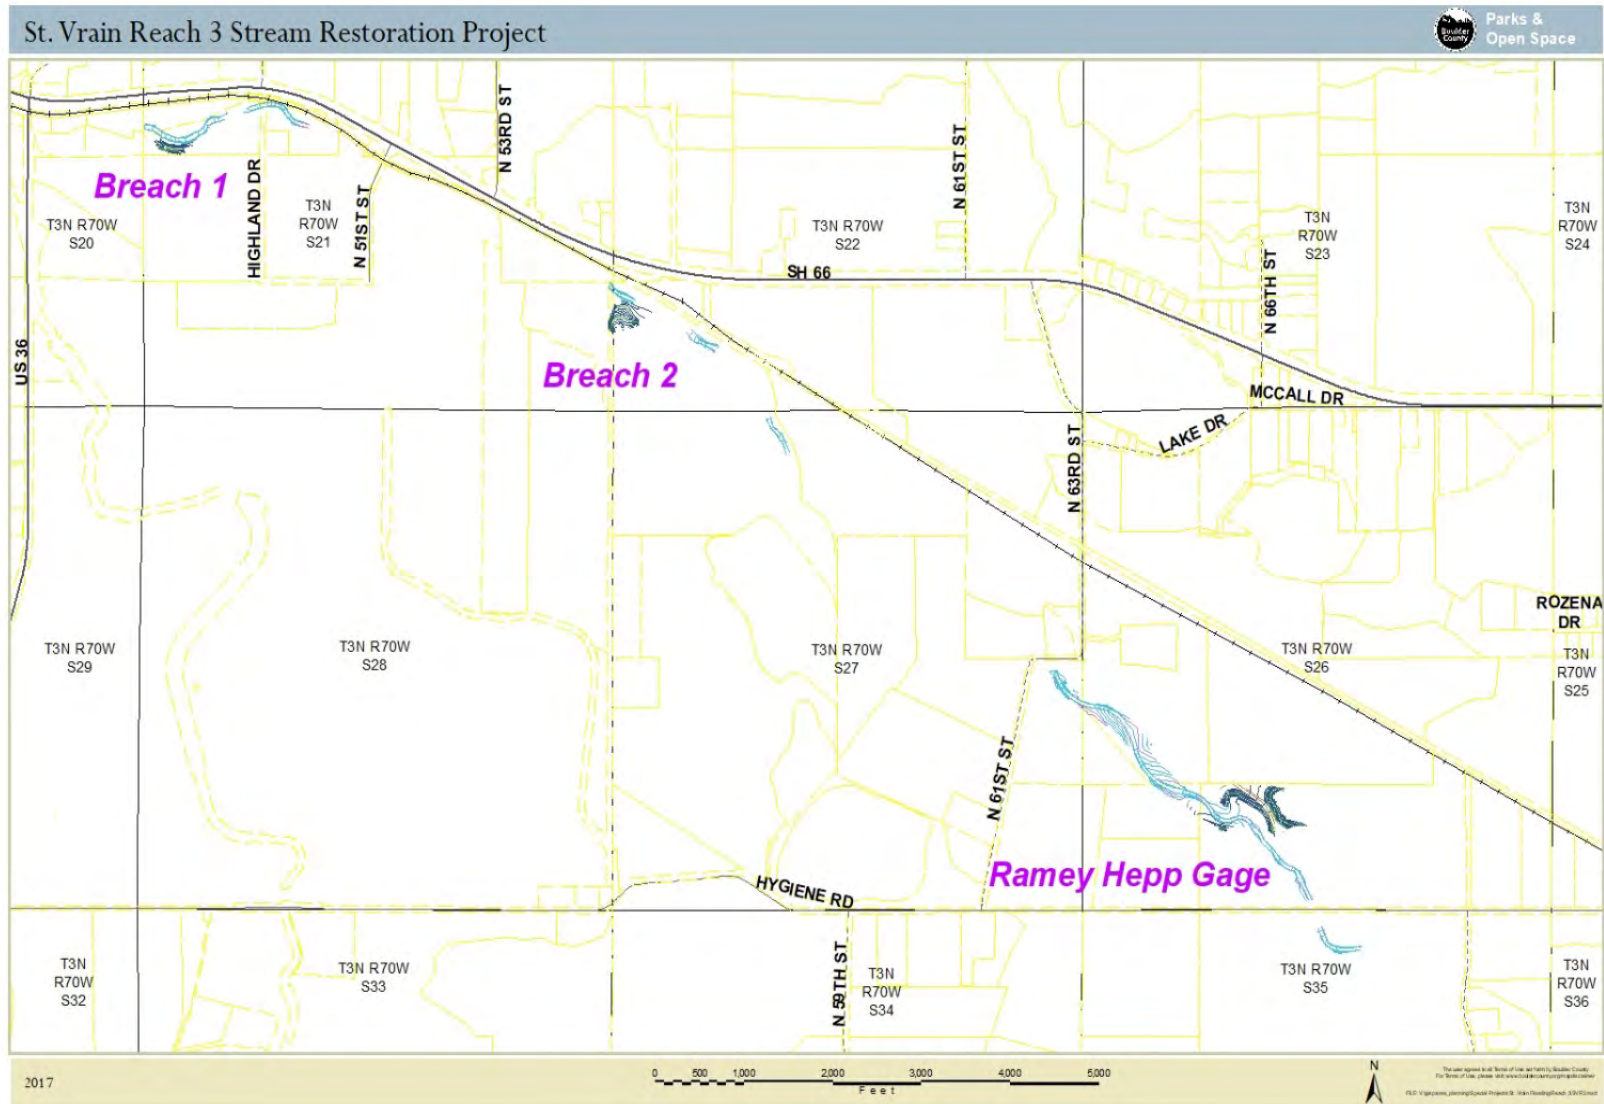

Work Locations Referenced: Gage, Hepp, and Ramey work sites
