| Activity ID | Activity Name | Original Duration | Early Start | Early Finish | Actual Start | Actual Finish |
|---|---|---|---|---|---|---|
| **St. Vrain Reach 3 March Update** | | 213 | 10-Apr-18 | 25-May-18 | 20-Sep-17 | |
| **Administrative** | | 150 | 10-Apr-18 | 24-May-18 | 20-Sep-1 | |
| A1000 | Notice to Proceed | 0 | 10-Apr-18 | 10-Apr-18 | 20-Sep-1 | 20-Sep-1 |
| A1010 | Permit Process | 38 | 10-Apr-18 | 10-Apr-18 | 21-Sep-1 | 27-Oct-17 |
| A1020 | Permits Complete | 1 | 10-Apr-18 | 10-Apr-18 | 30-Oct-17 | 30-Oct-17 |
| A1030 | Survey | 40 | 10-Apr-18 | 24-May-18 | 25-Sep-1 | |
| A1040 | Mobilization, Staging & Access | 5 | 10-Apr-18 | 10-Apr-18 | 24-Oct-17 | 30-Oct-17 |
| A1050 | Planting Winter Shutdown | 45 | 10-Apr-18 | 10-Apr-18 | 31-Oct-17 | 10-Mar-18 |
| **Breaches 6, 7a, 7b, 8 & 9** | | 137 | 10-Apr-18 | 10-May-18 | 25-Oct-17 | |
| A2000 | Breach Work 7 | 22 | 10-Apr-18 | 10-Apr-18 | 02-Nov-1 | 30-Jan-18 |
| A2010 | Install Erosion Control Items | 4 | 10-Apr-18 | 10-Apr-18 | 25-Oct-17 | 31-Oct-17 |
| A2020 | Clear & Grub | 4 | 10-Apr-18 | 10-Apr-18 | 02-Nov-1 | 07-Nov-1 |
| A2030 | Breach 7 Excavation and Clay Core Work | 14 | 10-Apr-18 | 10-Apr-18 | 13-Nov-1 | 03-Jan-18 |
| A2040 | Grading & Embankment | 14 | 10-Apr-18 | 10-Apr-18 | 14-Nov-1 | 12-Jan-18 |
| A2050 | Bank Stabilization C 2 | 4 | 10-Apr-18 | 10-Apr-18 | 01-Jan-18 | 25-Jan-18 |
| A2060 | Stream Channel Restoration 3 - 7 | 10 | 10-Apr-18 | 10-Apr-18 | 28-Nov-1 | 25-Jan-18 |
| A2070 | Type H Riprap | 10 | 10-Apr-18 | 10-Apr-18 | 02-Jan-18 | 08-Feb-18 |
| A2080 | Move Creek Station 38+00 - 34+00 | 1 | 10-Apr-18 | 10-Apr-18 | 25-Jan-18 | 26-Jan-18 |
| A2090 | Breach 6 Excavation and Clay Core Work | 7 | 10-Apr-18 | 10-Apr-18 | 24-Jan-18 | 22-Mar-18 |
| A2100 | Grading | 7 | 10-Apr-18 | 10-Apr-18 | 23-Mar-1 | 30-Mar-18 |
| A2110 | Move Creek Final Alignment | 1 | 10-Apr-18 | 10-Apr-18 | 26-Jan-18 | 26-Jan-18 |
| A2120 | Bank Stabilization D 5 - 6 | 16 | 10-Apr-18 | 10-Apr-18 | 25-Jan-18 | 31-Jan-18 |
| A2130 | Stream Channel Restoration 10 - 12 | 12 | 10-Apr-18 | 10-Apr-18 | 25-Jan-18 | 14-Mar-18 |
| A2140 | Bank Stabilization C 7 - 8 | 3 | 10-Apr-18 | 10-Apr-18 | 06-Feb-1 | 05-Mar-18 |
| A2150 | Stream Channel Restoration 13 | 3 | 10-Apr-18 | 10-Apr-18 | 02-Mar-1 | 09-Mar-18 |
| A2160 | Bank Stabilization Mod C 4 | 5 | 10-Apr-18 | 10-Apr-18 | 23-Mar-1 | 30-Mar-18 |
| A2170 | Stream Channel Restoration 8 - 9 | 5 | 10-Apr-18 | 10-Apr-18 | 23-Mar-1 | 30-Mar-18 |
| A2180 | Topsoil | 15 | 10-Apr-18 | 13-Apr-18 | 18-Dec-1 | |
| A2190 | Vegetation | 15 | 17-Apr-18 | 07-May-18 | | |
| A2200 | Plantings | 18 | 17-Apr-18 | 10-May-18 | | |
| **Gage Access Bank Stabilization** | | 118 | 10-Apr-18 | 14-May-18 | 26-Oct-17 | |
| A3000 | Type A Bank Stabilization 13+95 - 18+60 | 10 | 10-Apr-18 | 10-Apr-18 | 16-Nov-1 | 15-Dec-1 |
| A3010 | Install Erosion Control Items | 2 | 10-Apr-18 | 10-Apr-18 | 26-Oct-17 | 09-Nov-1 |
| A3020 | Clear & Grub | 2 | 10-Apr-18 | 10-Apr-18 | 13-Nov-1 | 15-Nov-1 |
| A3030 | Stream Channel Restoration 1 & 2 | 8 | 10-Apr-18 | 10-Apr-18 | 16-Nov-1 | 29-Dec-1 |
| A3040 | Topsoil | 2 | 10-Apr-18 | 10-Apr-18 | 18-Dec-1 | 20-Dec-1 |
| A3050 | Seed Supply | 7 | 10-Apr-18 | 10-Apr-18 | 21-Dec-1 | 13-Feb-18 |
| A3060 | Plant Deliveries | 5 | 10-Apr-18 | 12-Apr-18 | 10-Apr-18 | |
| A3070 | Vegetation | 2 | 13-Apr-18 | 16-Apr-18 | | |
| A3080 | Planting | 2 | 11-May-18 | 14-May-18 | | |
| **Ramey Stabilization** | | 4 | 08-May-18 | 11-May-18 | | |
| A4000 | Access Restoration | 2 | 08-May-18 | 09-May-18 | | |
| A4010 | Topsoil | 1 | 10-May-18 | 10-May-18 | | |
| A4020 | Vegetation | 1 | 11-May-18 | 11-May-18 | | |
| **Breach 1 and Bank Stabilization** | | 105 | 10-Apr-18 | 16-May-18 | 18-Dec-1 | |
| A5000 | Breach Work | 17 | 10-Apr-18 | 10-Apr-18 | 18-Dec-1 | 06-Feb-18 |
| A5010 | Install Erosion Control Items | 2 | 10-Apr-18 | 10-Apr-18 | 18-Dec-1 | 06-Feb-18 |
| A5020 | Clear & Grub Stockpile Riprap | 4 | 10-Apr-18 | 10-Apr-18 | 03-Jan-18 | 09-Jan-18 |
| A5030 | Excavation and Clay Core Work | 20 | 10-Apr-18 | 10-Apr-18 | 10-Jan-18 | 06-Feb-18 |
| A5040 | Grading | 20 | 10-Apr-18 | 10-Apr-18 | 12-Feb-1 | 14-Mar-18 |
| A5050 | Bank Stabilization B 15 | 12 | 10-Apr-18 | 10-Apr-18 | 19-Feb-1 | 07-Mar-18 |
| A5060 | Stream Channel Restoration 25 & 26 | 12 | 10-Apr-18 | 10-Apr-18 | 19-Feb-1 | 07-Mar-18 |
| A5070 | RR Agreement & Training | 22 | 10-Apr-18 | 12-Apr-18 | 07-Mar-1 | |

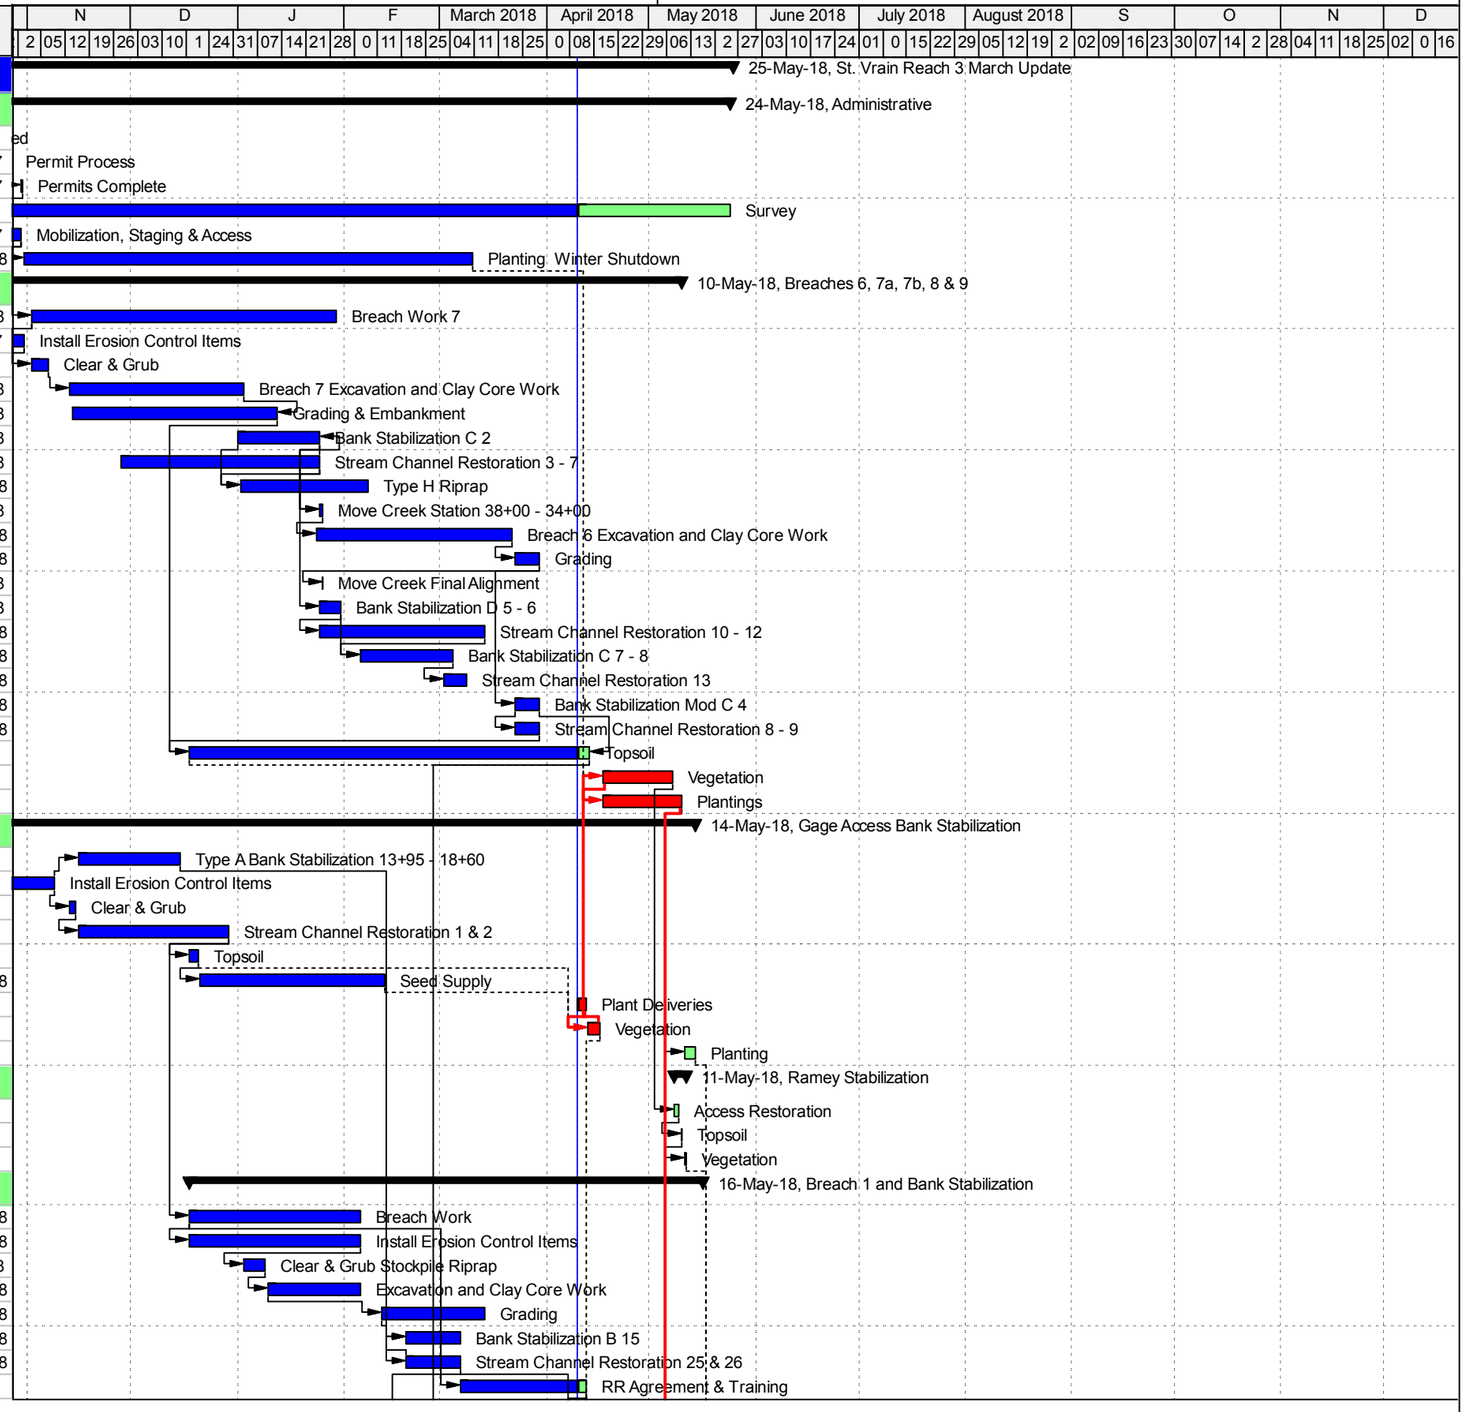


Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Original Duration | Early Start | Early Finish | Actual Start | Actual Finish |
|---|---|---|---|---|---|---|
| A5080 | Bank Stabilization A 14 | 7 | 13-Apr-18 | 23-Apr-18 | | |
| A5090 | Stream Channel Restoration 23 & 24 | 7 | 13-Apr-18 | 23-Apr-18 | | |
| A5100 | Topsoil | 10 | 16-Apr-18 | 24-Apr-18 | 05-Mar-' | |
| A5110 | Vegetation | 5 | 18-Apr-18 | 24-Apr-18 | | |
| A5120 | Plantings | 4 | 11-May-18 | 16-May-18 | | |
| **Breach 2 and Bank Stabilization** | | 41 | 10-Apr-18 | 25-May-18 | 21-Feb-' | |
| A6000 | Breach Work | 12 | 10-Apr-18 | 16-Apr-18 | 21-Feb-' | |
| A6010 | Install Erosion Control Items | 3 | 10-Apr-18 | 12-Apr-18 | 21-Feb-' | |
| A6020 | Clear & Grub | 5 | 12-Apr-18 | 12-Apr-18 | 22-Feb-' | 23-Feb-18 |
| A6030 | Excavation and Clay Core Work | 16 | 12-Apr-18 | 12-Apr-18 | 22-Mar-' | 29-Mar-18 |
| A6040 | Embankment & Grading | 16 | 12-Apr-18 | 12-Apr-18 | 22-Feb-' | 03-Apr-18 |
| A6050 | Bank Stabilization C 13 | 10 | 13-Apr-18 | 26-Apr-18 | 04-Apr-18 | |
| A6060 | Stream Channel Restoration 22 | 10 | 13-Apr-18 | 26-Apr-18 | 04-Apr-18 | |
| A6070 | Topsoil | 5 | 25-Apr-18 | 01-May-18 | | |
| A6080 | Vegetation | 5 | 30-Apr-18 | 04-May-18 | | |
| A6090 | Plantings | 4 | 17-May-18 | 22-May-18 | | |
| A6100 | Punchlist & Survey | 2 | 23-May-18 | 24-May-18 | | |
| A6110 | Project Completion | 0 | 25-May-18 | 25-May-18 | | |

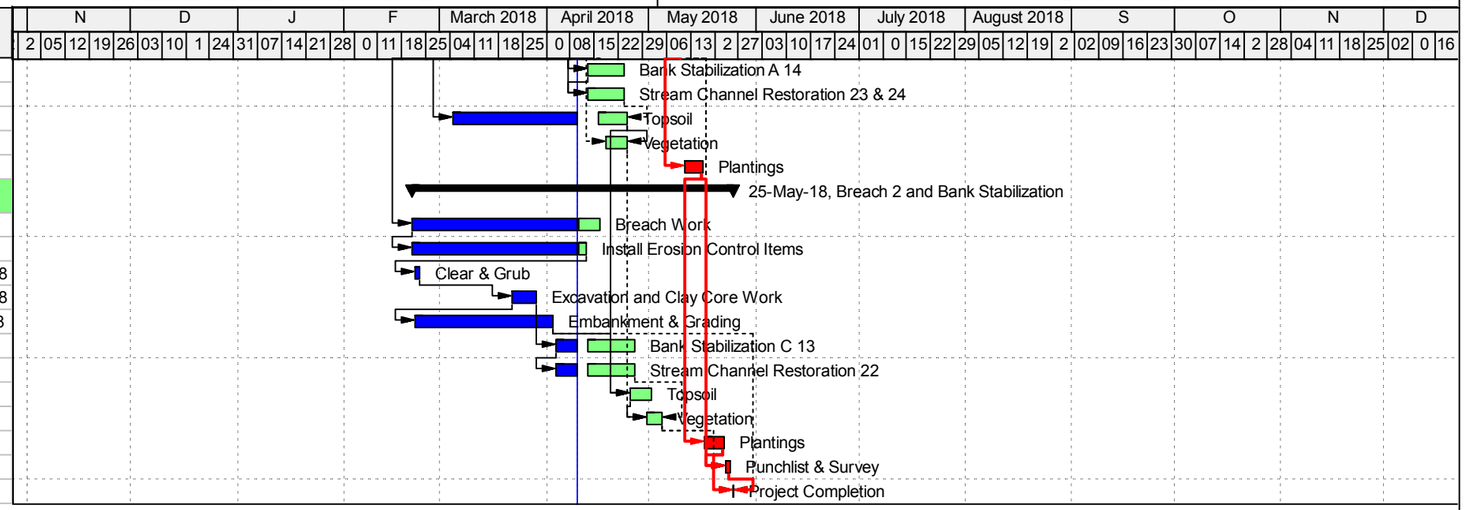



© Oracle Corporation
